






















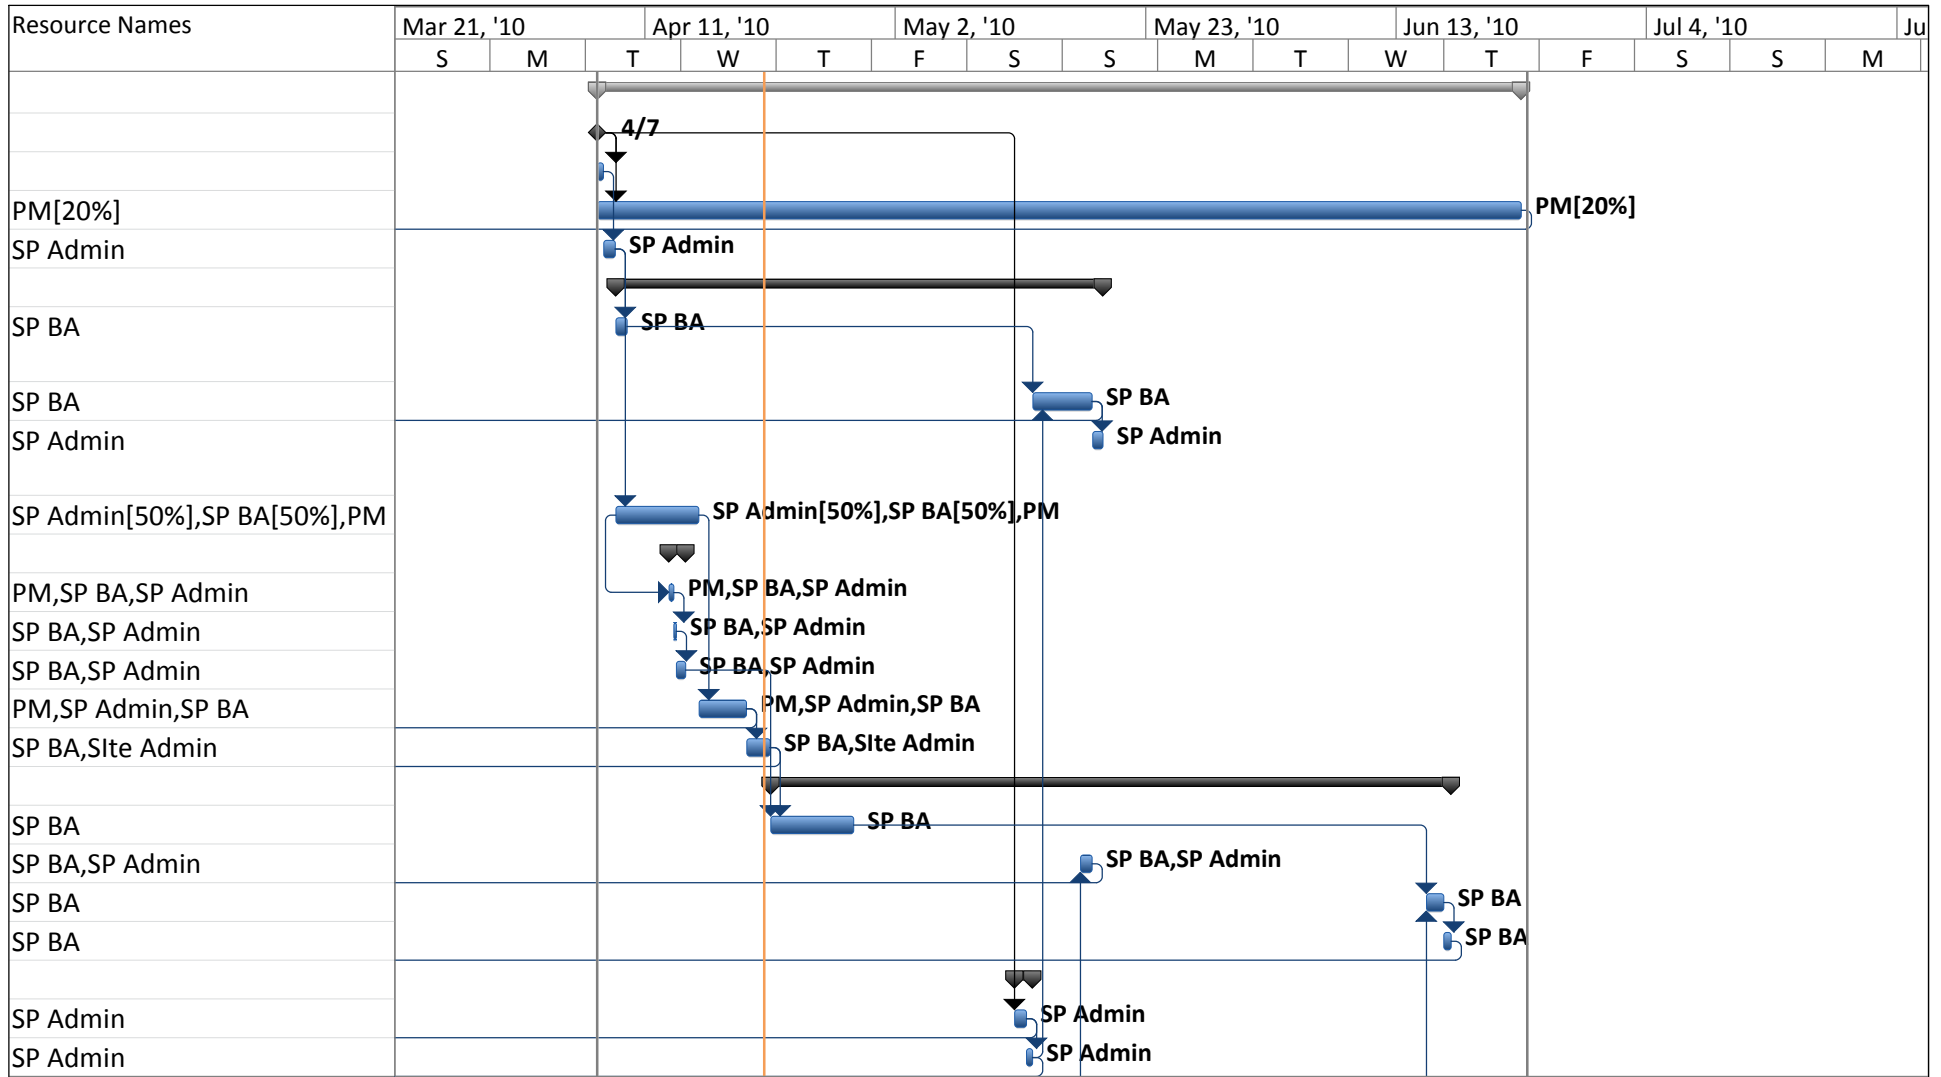


ID	Task Name	Duration	Work	Start	Finish	Predecessors
0	<b>IEC_SP2010_Migration_Schedule</b>	<b>55.5 days</b>	<b>961.05 hrs</b>	<b>Wed 4/7/10</b>	<b>Wed 6/23/10</b>	
1	Start	0 days	0 hrs	Wed 4/7/10	Wed 4/7/10	
2	Kickoff	0.5 days	0 hrs	Wed 4/7/10	Wed 4/7/10	1
29	Project Management	55.5 days	88.8 hrs	Wed 4/7/10	Wed 6/23/10	1
3	Create a Beta environment	1 day	8 hrs	Wed 4/7/10	Thu 4/8/10	2
7	<b>New Site Templates</b>	<b>28.75 days</b>	<b>38 hrs</b>	<b>Thu 4/8/10</b>	<b>Wed 5/19/10</b>	
8	Test Site template creation on Beta to RC1	1 day	8 hrs	Thu 4/8/10	Fri 4/9/10	3
9	Create 4 site templates	3 days	24 hrs	Thu 5/13/10	Tue 5/18/10	6,8
10	Update Site Collection to display only 4 site templates	0.75 days	6 hrs	Tue 5/18/10	Wed 5/19/10	9
18	Define governance policies	5 days	80 hrs	Thu 4/8/10	Thu 4/15/10	3
11	<b>User Management Planning</b>	<b>1.25 days</b>	<b>20.25 hrs</b>	<b>Tue 4/13/10</b>	<b>Wed 4/14/10</b>	
12	Identify Site Administrators	0.25 days	4.25 hrs	Tue 4/13/10	Tue 4/13/10	18SS+50%
13	Define SharePoint Groups	0.5 days	8 hrs	Tue 4/13/10	Tue 4/13/10	12
14	Define Site Membership Process	0.5 days	8 hrs	Tue 4/13/10	Wed 4/14/10	13
26	Content Migration Planning	2 days	48 hrs	Thu 4/15/10	Mon 4/19/10	18
24	Identify Referential Content for Portal	2 days	32 hrs	Mon 4/19/10	Wed 4/21/10	26
19	<b>Training</b>	<b>41.25 days</b>	<b>74 hrs</b>	<b>Wed 4/21/10</b>	<b>Thu 6/17/10</b>	
20	Create training materials	5 days	40 hrs	Wed 4/21/10	Wed 4/28/10	24,14
23	Create FAQ/Support Site	1 day	16 hrs	Mon 5/17/10	Tue 5/18/10	25
21	Train Site Admins	1.5 days	12 hrs	Tue 6/15/10	Wed 6/16/10	20,27
22	Train End Users	0.75 days	6 hrs	Thu 6/17/10	Thu 6/17/10	21
4	<b>New SP Environment</b>	<b>1.5 days</b>	<b>12 hrs</b>	<b>Wed 5/12/10</b>	<b>Thu 5/13/10</b>	
5	Create New SP Server Instance	1 day	8 hrs	Wed 5/12/10	Wed 5/12/10	1
6	Create 2 site collections	0.5 days	4 hrs	Thu 5/13/10	Thu 5/13/10	5


Project: IEC_SP2010_Migration_S Date: Wed 4/21/10	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID		Task Name	Duration	Work	Start	Finish	Predecessors
15		<b>Implement Site Taxonomy</b>	<b>5.5 days</b>	<b>52 hrs</b>	<b>Thu 5/13/10</b>	<b>Thu 5/20/10</b>	
17		Configure Ad-hoc Site Collection	1 day	4 hrs	Thu 5/13/10	Thu 5/13/10	5
16		Provision Departmental Sites	2 days	48 hrs	Tue 5/18/10	Thu 5/20/10	9,26
25		Create Portal	2 days	16 hrs	Thu 5/13/10	Mon 5/17/10	6,24
27		Migration of existing content	18 days	432 hrs	Thu 5/20/10	Tue 6/15/10	16
28		Testing	5 days	60 hrs	Tue 6/15/10	Tue 6/22/10	27,23,17
30		Finish	0 days	0 hrs	Wed 6/23/10	Wed 6/23/10	22,28,29

Project: IEC_SP2010_Migration_S Date: Wed 4/21/10	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	



Project: IEC_SP2010_Migration_S Date: Wed 4/21/10	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

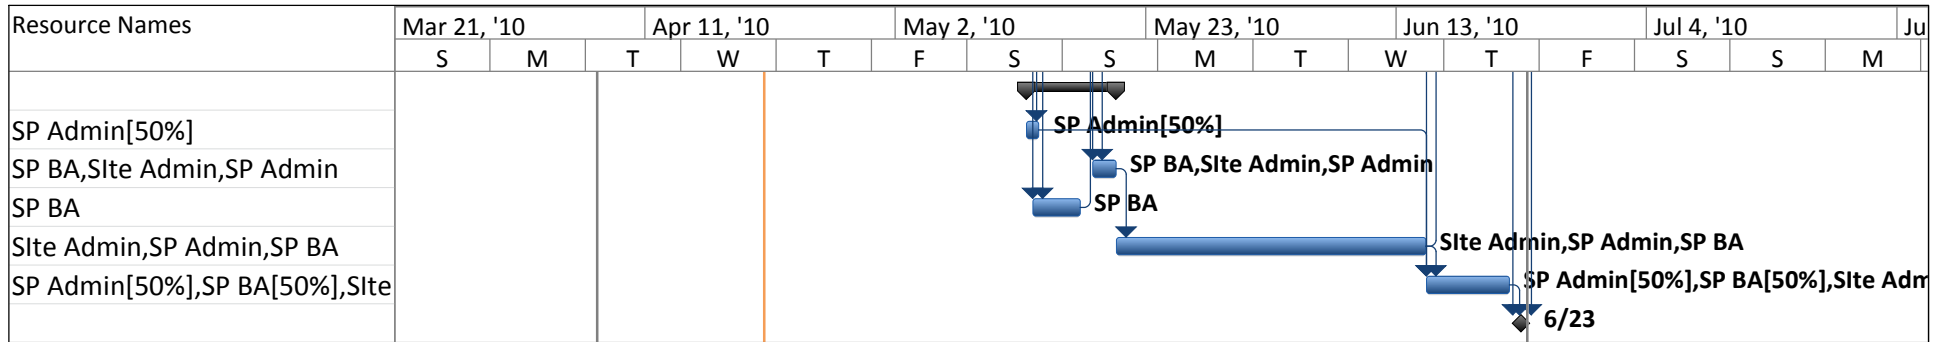

Project: IEC_SP2010_Migration_S Date: Wed 4/21/10	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
